



**East Midlands Gateway –
Electrical Infrastructure Works**


Matrix Networks Ltd is an accredited Independent Connections Provider. We're currently installing electrical infrastructure between the East Midlands Gateway development (J24 M1) and the Western Power Distribution supply point south of Stapleford. The total distance of these works is 12.5km

**November/December 2017
Update**

Our highway operations will cease for the festive season, between 4th December 2017 and 3rd January 2018.

Cable installation is planned for February 2018

We'll continue to keep local residents informed about any work which might affect their local area - and thank them for their patience.

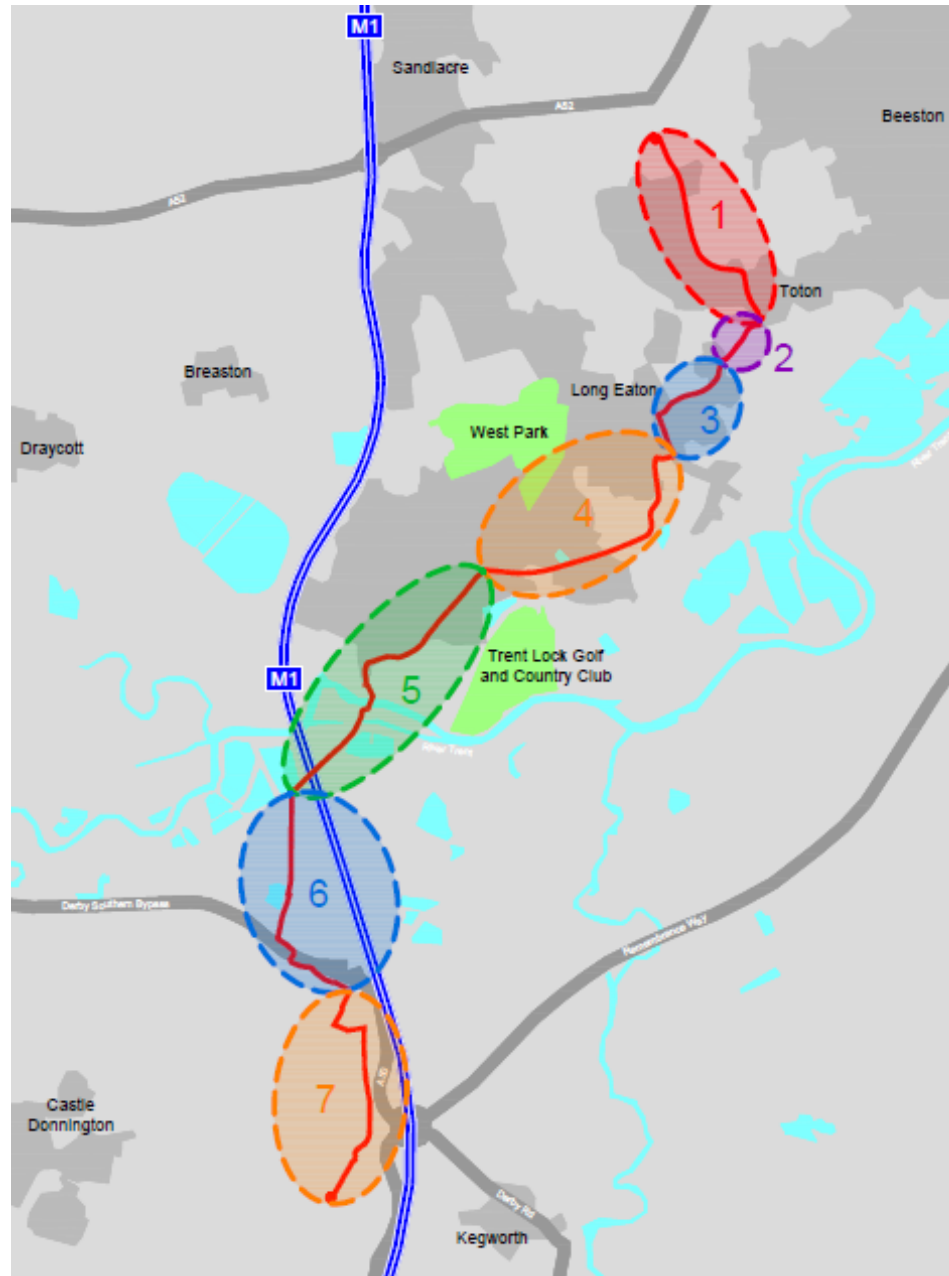

Section 1 –Stapleford Lane / High Road
Ducting installation – 95% complete. Excavation and duct laying - January 2018
Section 2 - Nottingham Road
Ducting installation 48% complete Excavation and duct laying - January 2018 Directional Drill - January 2018
Section 3 – Station Road – New Tythe St
Ducting installation Complete
Section 4 – Main street – Fields Farm Rd
Ducting installation 70% complete Excavation and duct laying - January 2018 Directional Drill - February 2018
Section 5 - Tamworth Road
Ducting installation 95% complete Excavations and duct laying -January 2018 Directional Drill – Feb 2018
Section 6 – Netherfield Lane
Ducting installation 85% complete Excavations and duct laying -February 2018 Directional Drill March 2018
Section 7 – Main Street to Site
Excavation and Duct Laying – March 2018

This is an indicative plan, for up-to-date traffic information please visit traffic England’s web page for precise traffic information: www.trafficengland.com or roadworks.org
To contact Matrix Networks Limited Major projects team, please email: EMG@matrixnetworks.co.uk Project Manager: Dave Foster :-0844 74 000 74
