


KEGWORTH BYPASS SUMMARY WORKS PROGRAMME

15TH SEPTEMBER 2017 – 31ST OCTOBER 2018

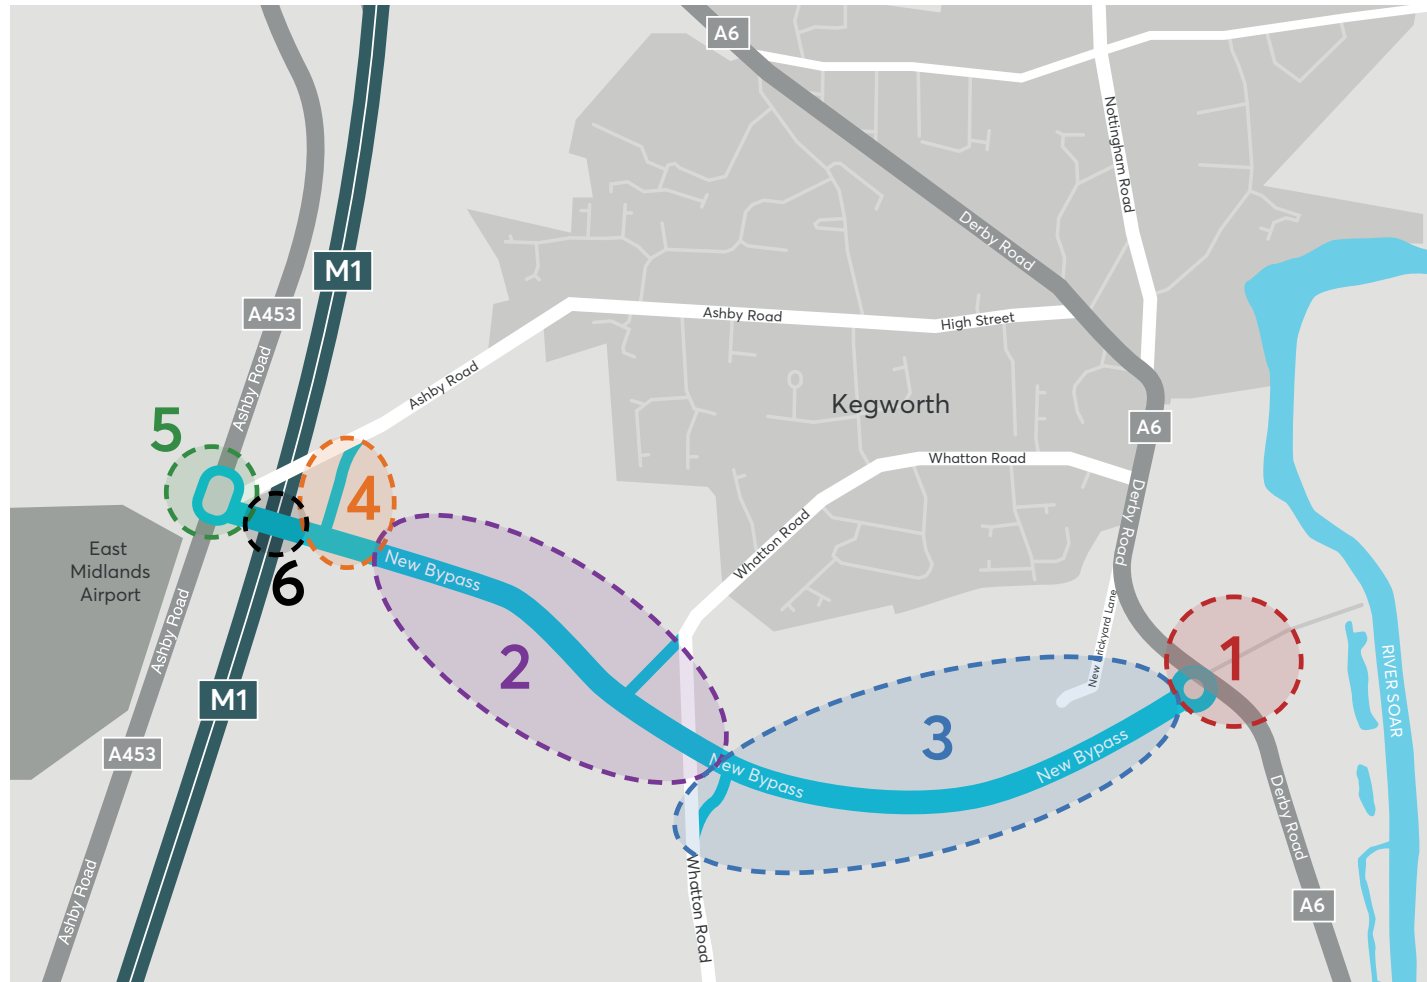

This is an indicative plan for up-to-date traffic information please visit traffic England's web page for precise traffic information; www.trafficengland.com or roadworks.org To contact Buckingham Group Contracting limited construction team please email: kegworthbypass@buckinghamgroup.co.uk

SECTION 1 - A6 London Road

Total Construction Period	113 Days
15 Sept 2017 - 06 Mar 2018	

SECTION 2 - Ashby Lane - Whatton Road

Construction Period	102 Days
19 Sept 2017 - 21 Feb 2018	

SECTION 3 - A6 - Whatton Road

Total Construction Period	113 Days
17 Oct 2017 - Early April	

SECTION 4 - Ashby Road

Bridge Fabrication	25 Days
17 Nov 2017 - 11 Dec 2017	

Post bridge tie in	37 Days
15 Jun 2018 - 6 Aug 2018	

Total Construction Period	118 Days
17 Nov 2017 - 6 Aug 2018	

SECTION 5 - Bridge to A453

Total Construction Period	52 Days
23 May 2018 - 3 Aug 2018	

SECTION 6 - M1 Overbridge

Abutment construction	Approx 25 Days
2 Oct 2017 to mid Feb 2018	

Offline deck construction period	72 Days
5 Feb 2018 - 18 May 2018	

Bridge launch	5 Days
21 May 2018 - 25 May 2018	

Bridge completion	5 Weeks
29 May 2018 - 2 Jul 2018	

Total Construction Period	189 Days
02 Oct 2017 - 2 Jul 2018	

COMPLETION WORKS

Total Construction Period	62 Days
6 Aug 2018 - 31 Oct 2018	
